Project Cost

DLZ Michigan, Inc. proposes to provide the professional surveying services outlined in this RFP for a lump-sum fee of One Hundred Twenty Six Thousand Dollars ($126,800.00). DLZ understands the scope and requirements of the St. Joseph County Survey RFP and is committed to delivering the requested services in a timely, efficient, and cost-effective manner for the stipulated lump-sum amount.

Project Schedule


DLZ has developed a project schedule that outlines key tasks, milestones, and deliverables to ensure the survey services are completed efficiently and within the County's desired timeframe. We are committed to meeting the schedule presented and maintaining clear communication throughout the project.

ST. JOSEPH COUNTY, MICHIGAN - INDIANA STATE LINE REMONUMENTATION PROJECT

Proposed Planning Schedule Gantt Chart | NTP November 1, 2026 | Required Completion December 31, 2027

Dates are proposal planning dates and should be refined with the County following written Notice to Proceed. Field activities account for seasonal access, leaf-off conditions, agricultural operations, water levels, and weather.

ID	Task	Phase	Start	Finish
1	Kickoff / contract execution / detailed work plan	Project Management	Nov 1, 2026	Nov 13, 2026
2	Historical research and record compilation	Research	Nov 1, 2026	Jan 15, 2027
3	Indiana records review and comparison framework	Research	Nov 16, 2026	Jan 29, 2027
4	Landowner / agency coordination and access planning	Coordination	Nov 9, 2026	Mar 12, 2027
5	Leaf-off reconnaissance and control recovery: Mile Posts 54-60	Field Investigation	Dec 1, 2026	Feb 26, 2027
6	Quarterly progress update #1	Reporting	Jan 29, 2027	Jan 29, 2027
7	Reconnaissance and control recovery: Mile Posts 61-70	Field Investigation	Feb 1, 2027	Apr 30, 2027
8	Evidence validation and preliminary retracement: Mile Posts 54-60	Analysis	Feb 15, 2027	Apr 16, 2027
9	Reconnaissance and control recovery: Mile Posts 71-79	Field Investigation	Mar 15, 2027	Jun 18, 2027
10	Quarterly progress update #2	Reporting	Apr 30, 2027	Apr 30, 2027
11	Evidence validation and preliminary retracement: Mile Posts 61-70	Analysis	Apr 5, 2027	Jun 25, 2027
12	Evidence validation and preliminary retracement: Mile Posts 71-79	Analysis	May 17, 2027	Jul 30, 2027
13	Supplemental research / focused verification of uncertain positions	Field Investigation	May 3, 2027	Aug 27, 2027
14	Peer-group / Commission coordination and discrepancy resolution	Review / Submittal	Jun 14, 2027	Sep 17, 2027
15	Quarterly progress update #3	Reporting	Jul 30, 2027	Jul 30, 2027
16	Remonumentation and post installation	Remonumentation	Aug 16, 2027	Oct 15, 2027
17	Final field documentation and monument verification	Documentation	Sep 1, 2027	Oct 29, 2027
18	Corner submission packages and review revisions	Review / Submittal	Aug 2, 2027	Oct 29, 2027
19	Quarterly progress update #4	Reporting	Oct 29, 2027	Oct 29, 2027
20	LCRC preparation, recordation, and distribution	Recordation	Oct 4, 2027	Nov 30, 2027
21	Final survey, Indiana comparison report, and electronic archive	Final Deliverables	Nov 1, 2027	Dec 17, 2027
22	Final QA/QC, County/State response, and project closeout	Final Deliverables	Dec 13, 2027	Dec 31, 2027
23	Required project completion	Milestone	Dec 31, 2027	Dec 31, 2027

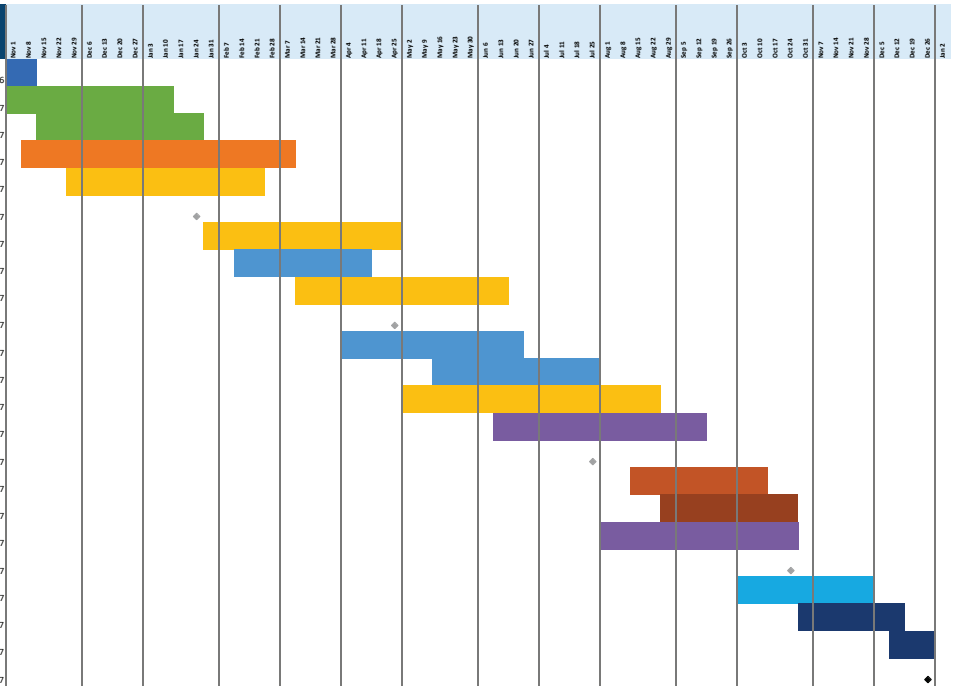

Personnel

Project Principal
Manoj Sethi, PE

Quality Manager
Tim Weir, PS

Steve A. Jones, PS, CFedS
Project Manager



Surveying
Doug Westgate, PS
Anthony Toscani, PS
Alex Huxhold, EI*

Field Crew Chief
Brian Todd, CST
Dylan Manuwal*

* Resume not included



Steven A. Jones PS, CFedS

Director of Survey



Steve has 30 years of technical and project management experience in performing horizontal and vertical control surveys, boundary surveys, route surveys, hydrographic surveys, and topographical surveys. He has been responsible for the implementation and training of personnel in surveying technologies such as GPS, laser scanning (LiDAR), and Unmanned Aerial Systems. As a Certified Federal Surveyor, Steve has specialized training in the U.S. Public Land Survey System, and boundary determination.

Project Experience

Indiana-Michigan State Line. *Survey Project Manager*. Responsible for the research, recovery, survey, and perpetuation of 45 milepost monument positions along the Indiana-Michigan state line. Tasks included analyzing the original government plats/field notes; searching for remaining evidence of bearing trees; searching for memorials; analyzing topographic features; re-establishing lost and obliterated monuments; analyzing public land survey corners in relation to opinion monuments and improvements; creating drawings detailing findings that show the state plane coordinates and latitude/longitude of each surveyed point. (2021-2024)

Indiana-Michigan State Line Cost Study. *Survey Project Manager*. Responsible for the research and analysis of effort and expenses necessary for the perpetuation of 105 milepost monument positions along the State Line from Lake Michigan to the Ohio border. (2024)

State Line Section Corner Perpetuation, LaPorte County, Indiana. *Survey Project Manager*. Responsible for the recovery, survey, and perpetuation of 25 public land section corner monument positions along the Indiana-Michigan State Line throughout LaPorte County. (2022)

USDA/NRCS IDIQ Boundary Surveys, Various Counties, Indiana. *Survey Project Manager*. Responsible for the boundary surveys of several sites in 20 Counties across Indiana. Retracement surveys involved boundary determination of conservation areas and Public Land section corner perpetuation. Deliverables included field staking of the lines, setting of signposts, and preparation of a signed and sealed Plat of Survey, showing State Plane Coordinates and Latitude/Longitude for all survey corners, as well as developing GIS files of the easements. (2022-2024)

Fort Custer VA Cemetery, Augusta, Michigan. *Survey Project Manager*. Responsible for the topographical survey of the 475 acre site for development of new cemetery sections. Project included the survey of 16,000 lineal feet of adjoining roadway. (2024)

Education

BS Construction Technology, Purdue University, 2002

AS Civil Engineering Technology, Purdue University, 1996

Registrations

Professional Surveyor:

Ohio, 8464, 2009

Missouri, 2010000244, 2010

Alabama, 30979, 2010

Indiana, 20200010, 2002

Wisconsin, 02660-, 2003

Illinois, 035003589, 2023

Michigan, 4001056304, 2009

Kentucky, 4359, 2020

Florida, LS6824, 2010

Tennessee, 3359, 2021

Colorado, 0038874, 2024

South Dakota, 17219, 2024

North Dakota, LS-40913, 2024

Minnesota, 63512, 2024

Texas, 7138, 2024

California, 10065, 2025

Certifications

OSHA 10-Hour Training

UAS – Remote PIC Certification

Safety – HAZWOPER 40 Hour Refresher

Affiliations

Indiana Society of Professional Land Surveyors

National Society of Professional Land Surveyors
